Network Open Season Project Updates

Central Ferry-Lower Monumental

Transmission Customer Forum 41

April 23, 2015

Pre-decisional. For Discussion Purposes Only.

Objective

- Provide status updates on projects resulting from the 2008, 2009 and 2010 Network Open Season (NOS) processes.

Pre-decisional. For Discussion Purposes Only.

Network Open Season Project Map

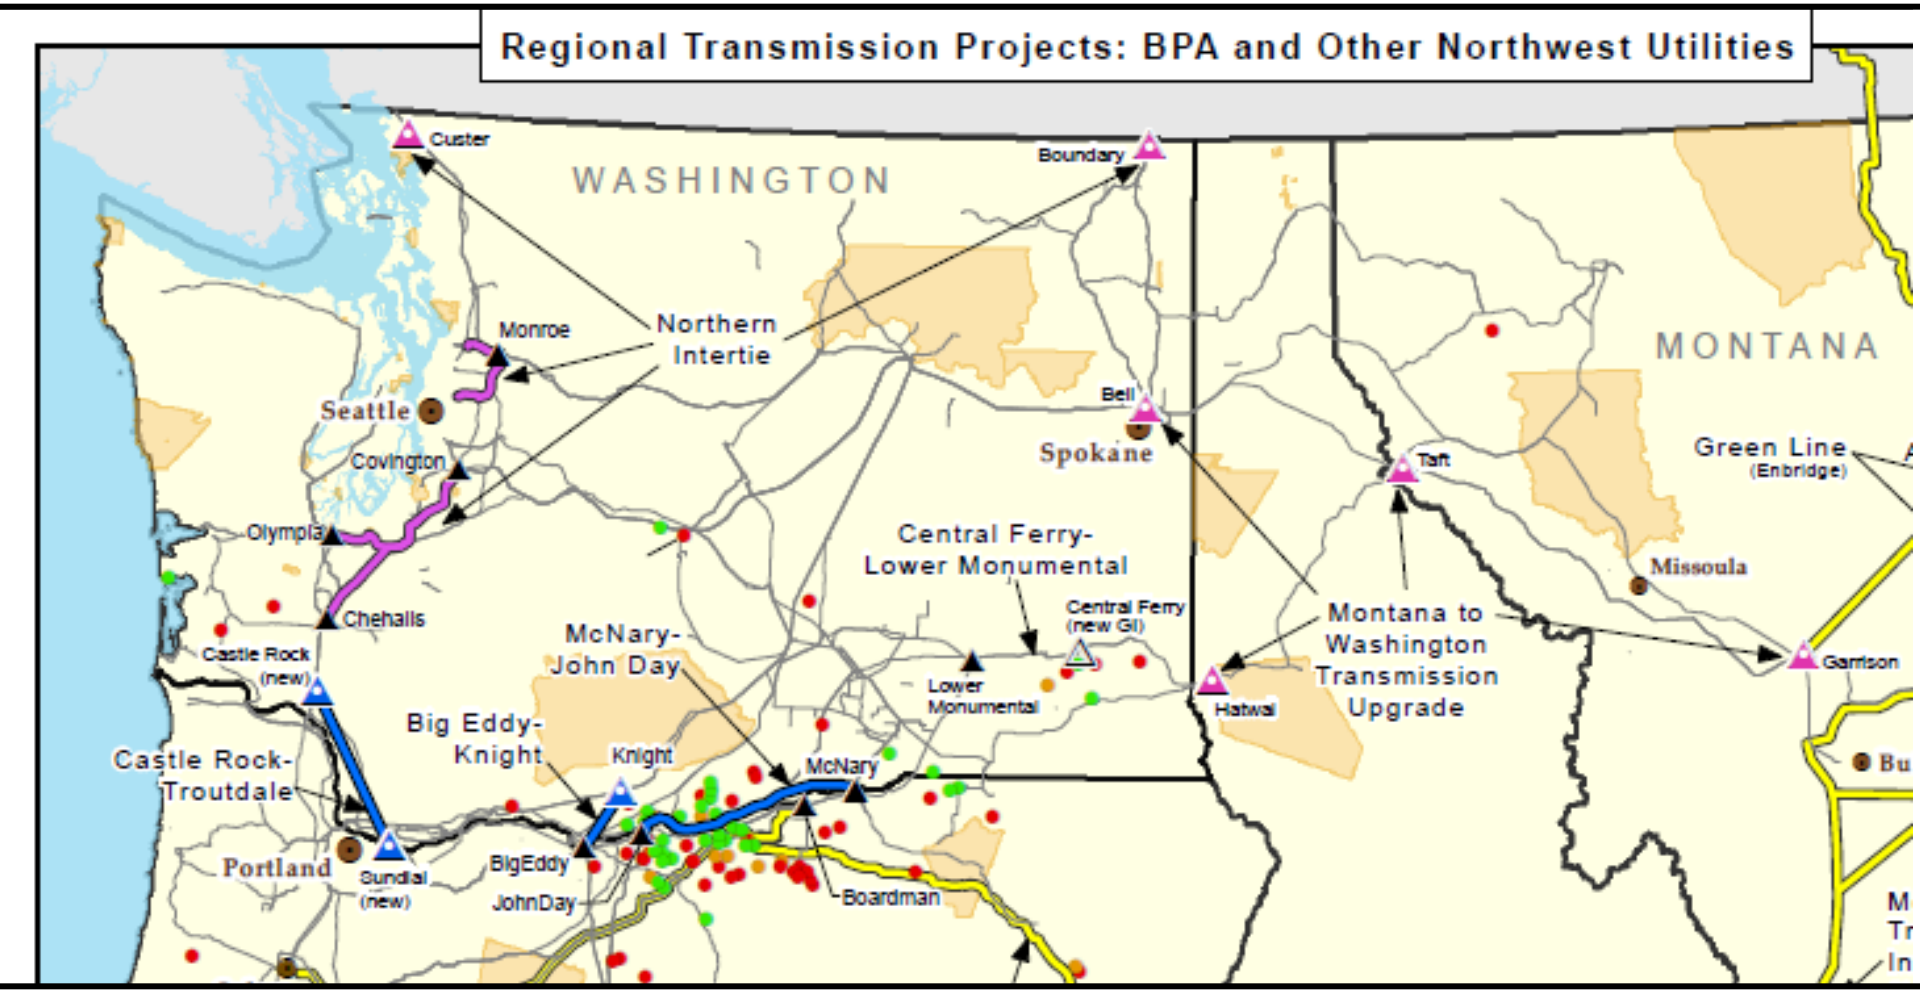

Pre-decisional. For Discussion Purposes Only.

Central Ferry-Lower Monumental

- Project Description
  - 40 miles new 500kV transmission line, Central Ferry and Lower Monumental Sub Bay Additions
- Schedule
  - 2009 Feb. - Project approved and launched
  - 2011 March - Final Environmental Impact Statement (EIS) and
  - Record of Decision (ROD)
  - 2011 Aug. - BPA Assesses Need Date
  - 2013 Aug. - BPA Resumes Work
  - 2014 Spring - Construction Start for Line and Substations
  - 2015 Feb. Substation Construction Substantially Completed
  - 2015 December - Project Energization for Line
- Budget
  - Total Project costs (Direct): $119.5 million
  - Actual costs to date (Direct) $90.2 million

Pre-decisional. For Discussion Purposes Only.

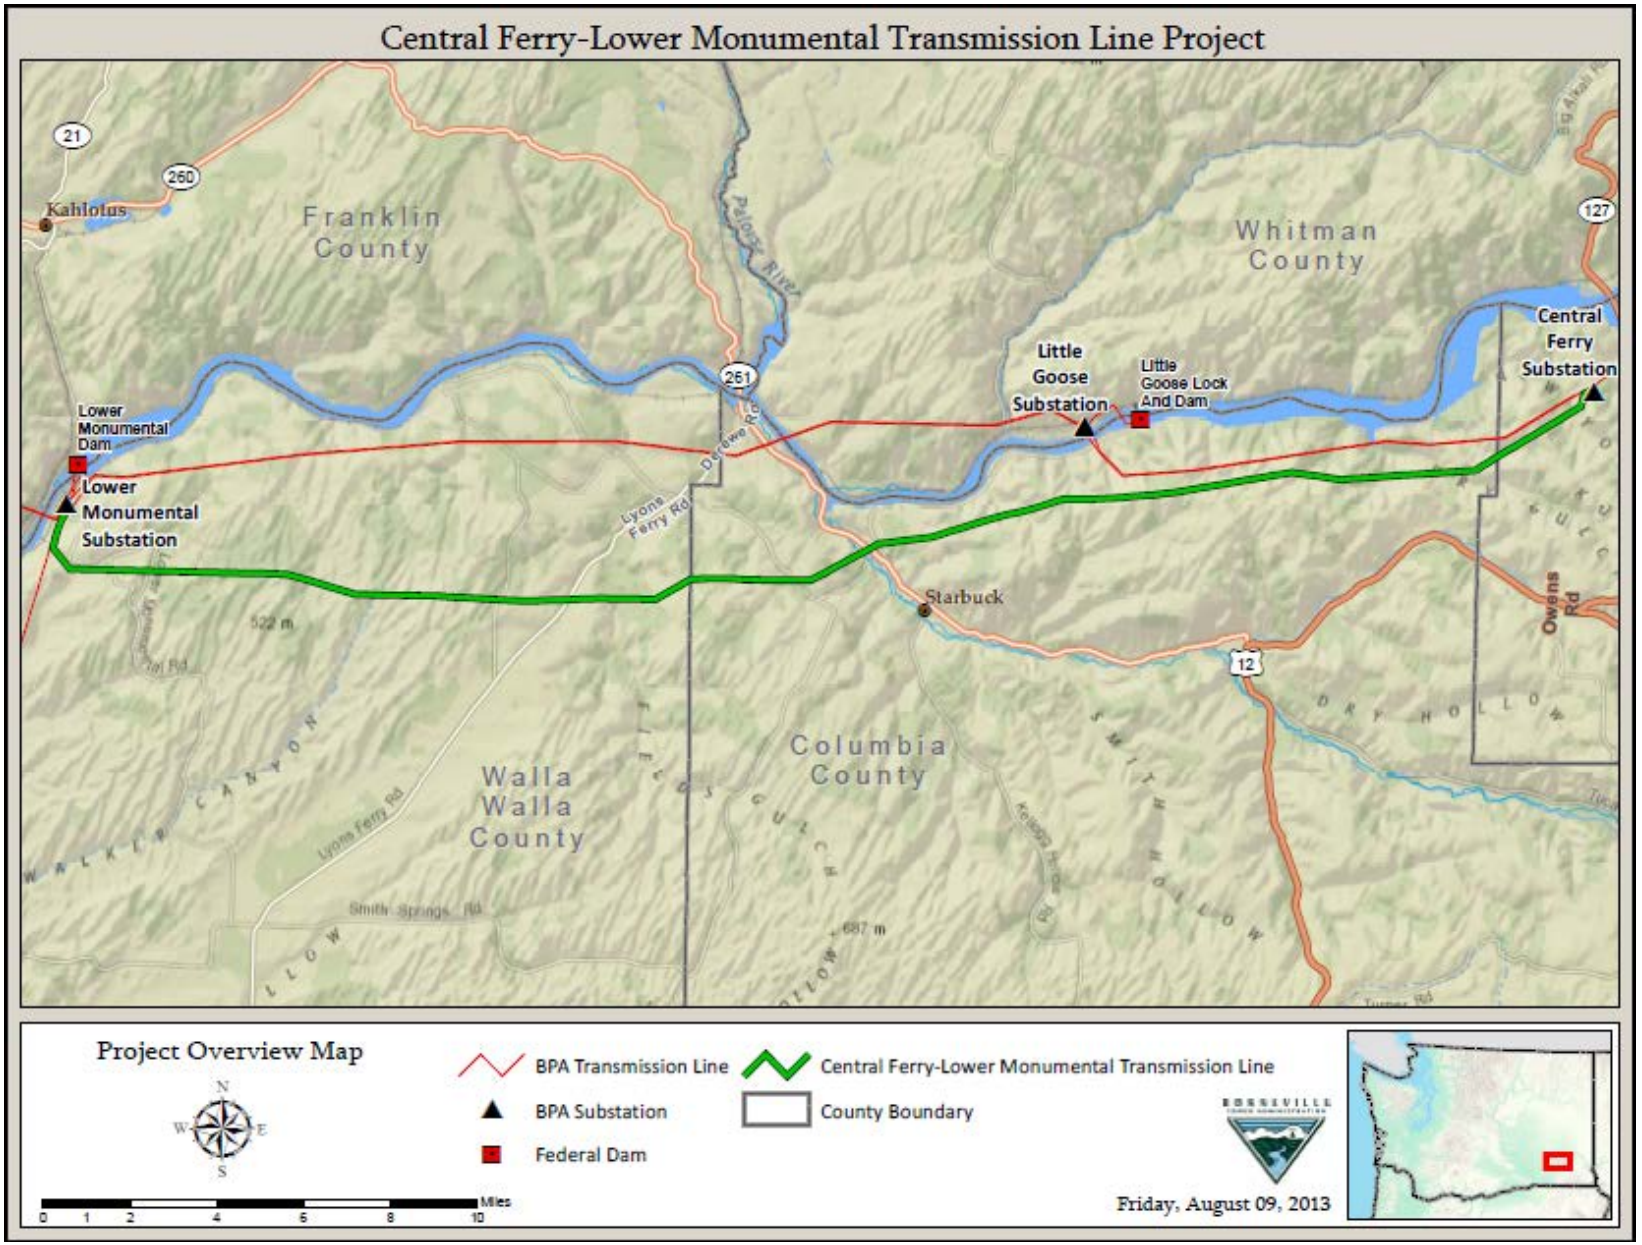

Pre-decisional. For Discussion Purposes Only.

Pre-decisional. For Discussion Purposes Only.

Pre-decisional. For Discussion Purposes Only.

Pre-decisional. For Discussion Purposes Only.

Pre-decisional. For Discussion Purposes Only.
